


Ryan Companies | Project Pearl



DIVISIONS

Garrett Electric
Olsson Industrial Electric
OS Engineering

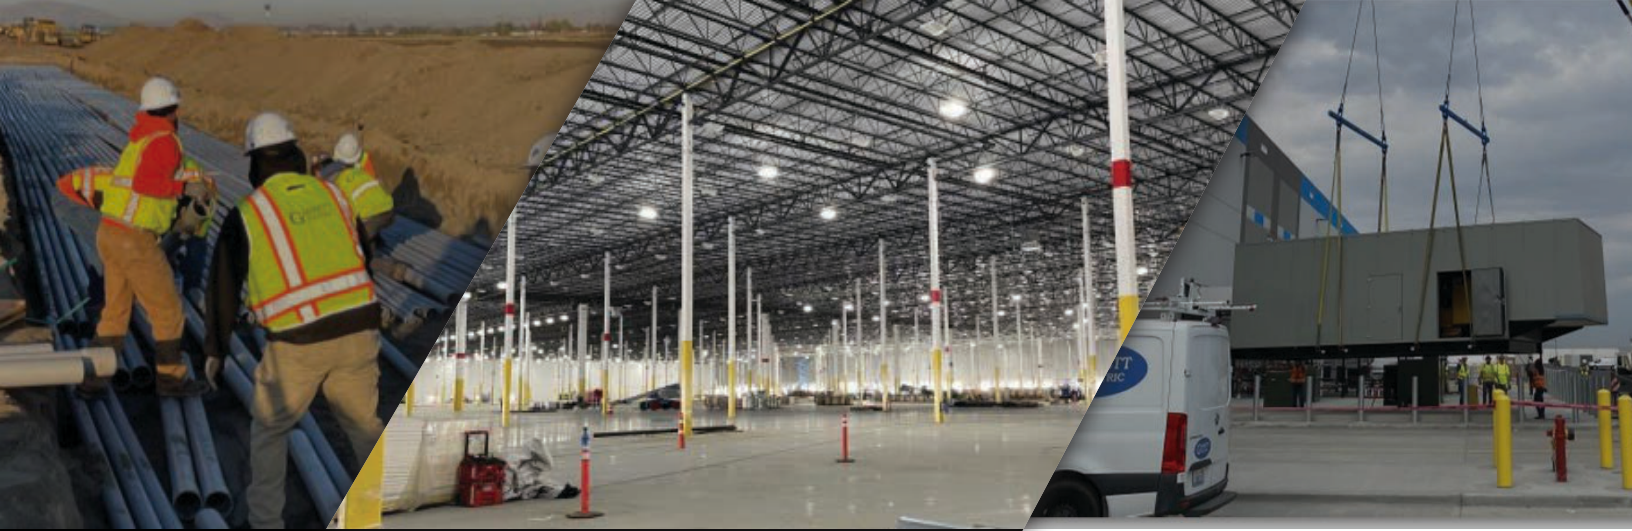

LOCATION

Pasco, WA



START DATE

September 2021



END DATE

In Progress

SCOPE OF WORK:

- New construction of a 1,028,000 SF online retail distribution center with 45-ft ceilings
- Included 20,000 SF office, fire pumphouse, and three guard stations
- Installed two 4,000-amp services for the main building and two for EV charging stations
- Installed 30 miles of underground and 25 miles of overhead conduit
- Completed electrical installation for 108 dock doors and levelers
